

CONSERVATION RECORD DOCUMENT
 Preventive Conservation / Conservation Works

Samma Noble I & II, Makli
1. WORK PLAN

 Name of Work:
 Provision of Temporary Supports

Area Makli, Thatta WHS4	Struct. Name. Samma Noble I & II	Struct. No. 1.08, 1.09
-------------------------------	--	--

World Heritage Site at Makli, Thatta – WHS4
Cluster 1, Samma Monuments

 Ref. Drg:
Under preparation
1.1 Description

Placing of bamboo supports to all the leaning and or badly damaged brick walls in subject structures i.e. Tomb of Samma Noble I and II. The propping was carried out using about 4" diameter bamboo poles placed on lime stone base with about 4" diameter and 1 ½ " deep seat so that bamboos are not in direct contact with earth. Similarly, 4" x 6" and about an inch thick timber packing was placed between the top of the bamboo and the wall bricks. The locations were on all four sides of the Tomb of Samma Noble I and on South & West walls of Samma Noble 2 as seen in photographs below.

1.2 Reason for Activity

The activity was undertaken in pursuance of the decisions taken in the site meeting held on 5th March 2012 by Ar. Yasmeen Lari, and Engr. Mushtaq Dawood in order to provide temporary support to the most vulnerable parts. Engr. Mushtaq Dawood had recommended the propping up by providing bamboo supports since several parts of the structures were found to be in an extremely critical state and it was feared that they could collapse any time. The temporary propping up was essential until the documentation process was completed and strategies for conservation could be worked out.

1.3 Time Frame

 Date of start:
 (Preparation)

Day	Month	Year
11	12	2012

 Date of finish:
 (Installation)

Day	Month	Year
12	12	2012

1.4 Workforce Requirement

No. 1	No. 2	No. 2	No. 1
Supervisor	Skilled	Semi-skilled	Unskilled

1.5 Estimated Cost

To be calculated.

1.6 Mechanism for recording material that may be removed

Not applicable. No material was removed except samples of mortar for testing purposes.

1.7 Methodology for identifying new works

The placement of temporary supports was carried out according to locations identified by Engr. Mushtaq Dawood.

1.8 Methodology for recording executed works


Photographic recording was carried out during execution.

1.9 Photographs Samma Noble I



Photographs by Engr. Mushtaq Dawood

1.10 Photographs Samma Noble II

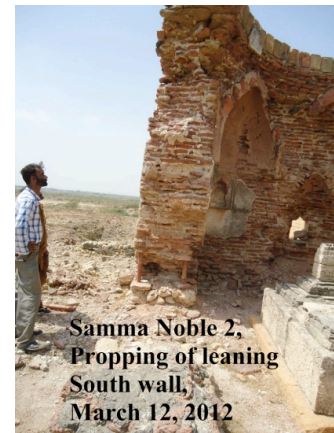

1.11 Form prepared by Ar. Yasmeen Lari

Date: 16 March, 2012

Designation

Hon. Project Director
CEO Heritage Foundation

Signature

